

CZBB Airside Capital Project Update

August 27th, 2015

1. 12-30 Lighting and Electrical Work

- Entered into contract with Continental Power Inc.
- Work has commenced for new taxi and runway lights to increase the landing distance for runway 30 to 4406 feet.
- Completion following civil work anticipated end of October.
- Aeronautical Publications to be updated.



Above is a new “pull pit” and grounding wire as well as locations for the new runway end lights.


2. Partial closure of Runway 12-30 and Displaced Threshold on 07

- Thank you to all tenants for your cooperation
- Thank you to Nav Canada for your coordination
- Please note displaced threshold markings below.



3. 12-30 Overlay and Taxi-lane Golf

- Delta in contract with Lafarge-Columbia Bitulithic.
- Work has commenced to prepare the concrete base for asphalt overlay
- Planned runway 12-30 closures and displaced threshold on 07-25 to be coordinated with electrical work.

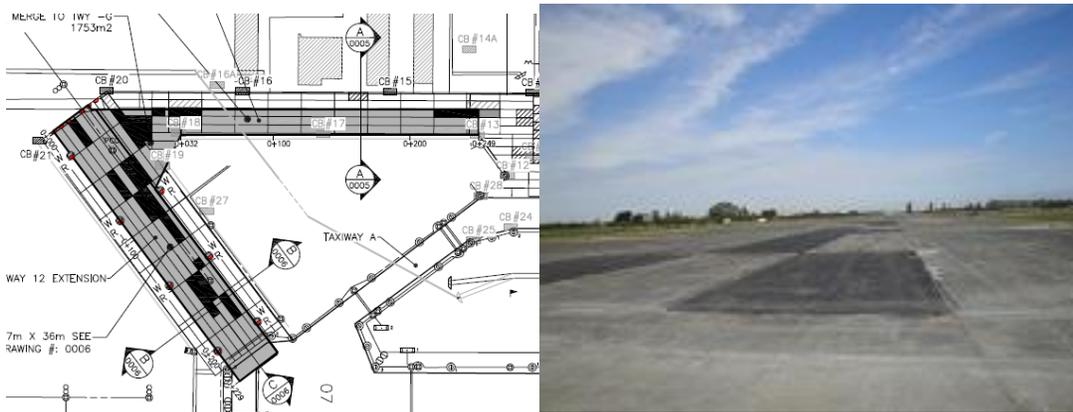

Note: identified panels have been replaced prior to completing the overlay.



Portions of the Golf Apron have been repaired prior to overlay of Taxi-lane Golf

4. King Street Apron

- Base is being prepared for a new apron which will tie in to the main apron
- New hangars under construction

