

## CZBB Airside Capital Project Update

June 10th, 2015

### 1. Apron 1 Rehabilitation

- Delta has contracted with Arsalan Construction Ltd. to complete rehabilitation of damaged concrete panels.
- The objective is to address FOD and improve movement areas. Only those panels that are severely damaged will be removed and those panels suitable for parking light aircraft will remain.
- Alpha Aviation Inc. would like to thank all tenants for their cooperation in moving aircraft during construction.
- Completion for the Apron work is expected in the first week of July.




## 2. Airfield Ditch Drainage (Parallel to 12-30)

- This work was completed by Delta crews.
- Creates separate airport drainage to allow 72<sup>nd</sup> street irrigation ditches to operate without back-flow to the airport



## 3. 12-30 Lighting and Electrical Work

- Alpha Aviation issued a Tender Package 11 May 2015 to three companies
- In step with the reactivation of the northern end of Runway 12-30 new LED lights will be installed for the whole length of the runway.
- This work is expected to start in early July.

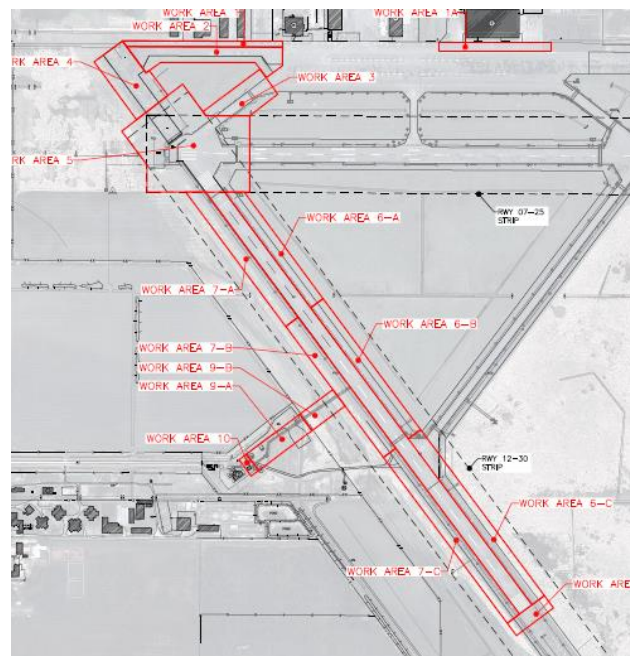

## 4. 12-30 Overlay and Taxi-lane Golf

- Tender for upgrades of runway 12-30 has been issued by Delta June 5<sup>th</sup>, 2015
- Work on this project is planned to start following the Airshow July 25<sup>th</sup>
